PROGRESSIVE COMPANIES

Harbor Transit

New Operations Center

Proposed Project Schedule

ID	Task Name	Duration	Start	Finish
1	NEPA	613 days	Wed 2/1/23	Fri 6/27/25
2	Kick off meeting	1 day	Tue 8/8/23	Tue 8/8/23
3	**Design**	**583 days**	**Wed 8/16/23**	**Fri 11/28/25**
4	**Concept Design**	**25 days**	**Wed 8/16/23**	**Tue 9/19/23**
5	Finalize building program	10 days	Wed 8/16/23	Tue 8/29/23
6	Determine adjacencies	5 days	Wed 8/30/23	Tue 9/5/23
7	Lay out site	10 days	Wed 9/6/23	Tue 9/19/23
8	Estimating	5 days	Wed 9/20/23	Tue 9/26/23
9	Harbor Transit review of Concept Package	5 days	Wed 9/27/23	Tue 10/3/23
10	Concept review meeting	1 day	Wed 10/4/23	Wed 10/4/23
11	Schematic Design	35 days	Tue 1/23/24	Mon 3/11/24
12	Estimating	10 days	Tue 3/12/24	Mon 3/25/24
13	Site Plan Approval - Grand Haven Township	70 days	Mon 6/9/25	Fri 9/12/25
14	Design development	40 days	Mon 6/9/25	Fri 8/1/25
15	Estimating	25 days	Mon 8/4/25	Fri 9/5/25
16	Construction documents	60 days	Mon 9/8/25	Fri 11/28/25
17	**Construction**	**375 days**	**Mon 12/1/25**	**Fri 5/7/27**
18	Bidding	20 days	Mon 12/1/25	Fri 12/26/25
19	Permitting - Grand Haven Township	30 days	Mon 12/1/25	Fri 1/9/26
20	Construction award/Board approval	20 days	Mon 12/29/25	Fri 1/23/26
21	Mobilization	10 days	Mon 3/2/26	Fri 3/13/26
22	Construction	300 days	Mon 3/16/26	Fri 5/7/27
23	Move in	15 days	Mon 5/10/27	Fri 5/28/27

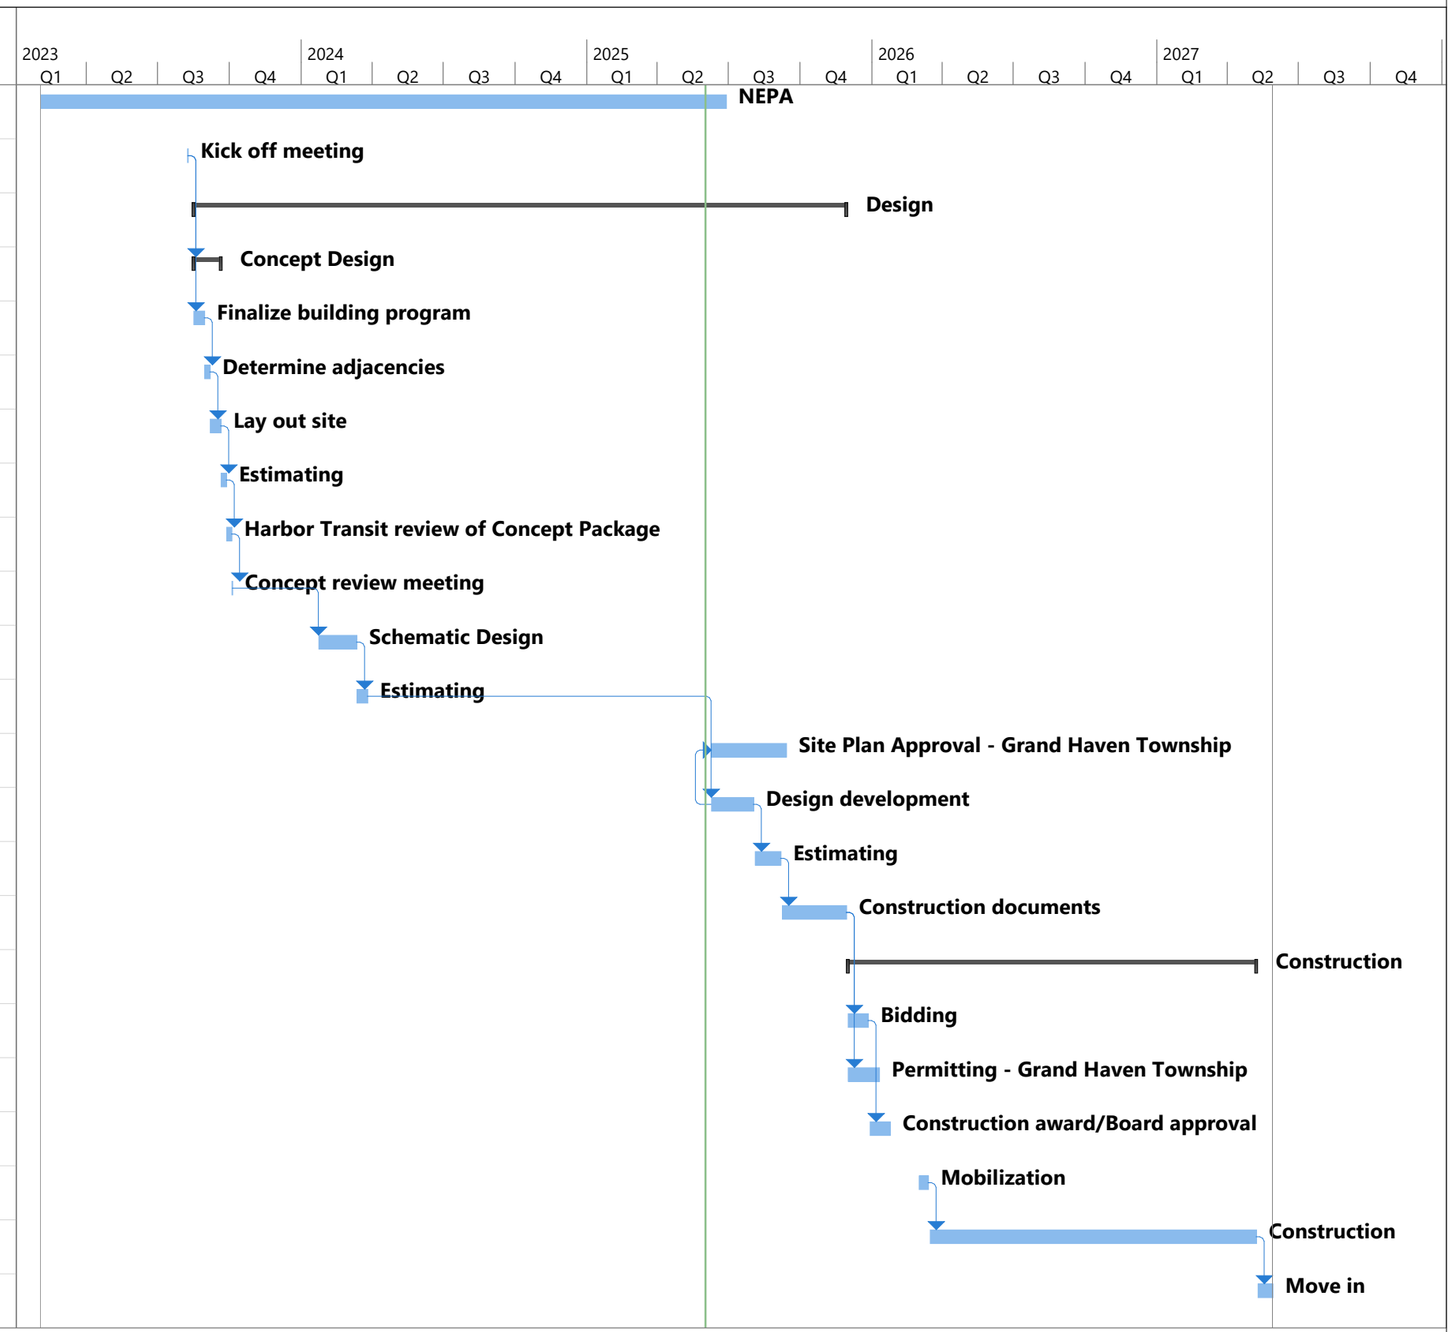

Mon 6/2/25
